



Citizen's Oversight Committee Meeting
Construction Update Overview, September 7, 2022

- ***Reconstruction of Chino HS***

The new Chino High School opened on Monday, August 8, 2022, with many cheers and bright smiles. Both Phase 1 and 2 continue to progress towards completion. Phase 1 is now in the punch list correction phase with various items and issues being addressed by contractors while the project management team and CVUSD begin to work on closeout. Work is ongoing in Phase 2 and is being done after school hours and on weekends to keep classroom disruption to a minimum. Major work in the theater, performing arts classrooms, and lecture hall will be wrapping up over the next few weeks, leaving only a few exterior tasks and the punch list to tackle. Phase 2 will continue onto the south side of the property as the previous site is demolished and space is being created for the site's new playfields. CVUSD continues to work with the City of Chino, SCE, and other utility providers on the offsite improvements surrounding the school, including paths of travel, undergrounding overhead lines, and creating safe streets.

Aerial View



Bldg. D Library




Bldg. H Theater



- ***Ayala HS Modernization***

Phase 4 Modernization is now underway with a completion date of August 2023. Work will take place in the administration building, gymnasium, and pool buildings, as well as to the pool and pool deck. Building A demolition is complete, with rough-in of electrical, data, and plumbing underway. The building is having the interior side of the entrance augmented to create a single point of entry. Site concrete around the building has also been demoed out with concrete scheduled to be poured this week. As with previous phases, this phase includes upgraded utility lines and security systems as well as new furniture and cabinetry, interactive technology, and ADA upgrades.


Ayala HS Administration

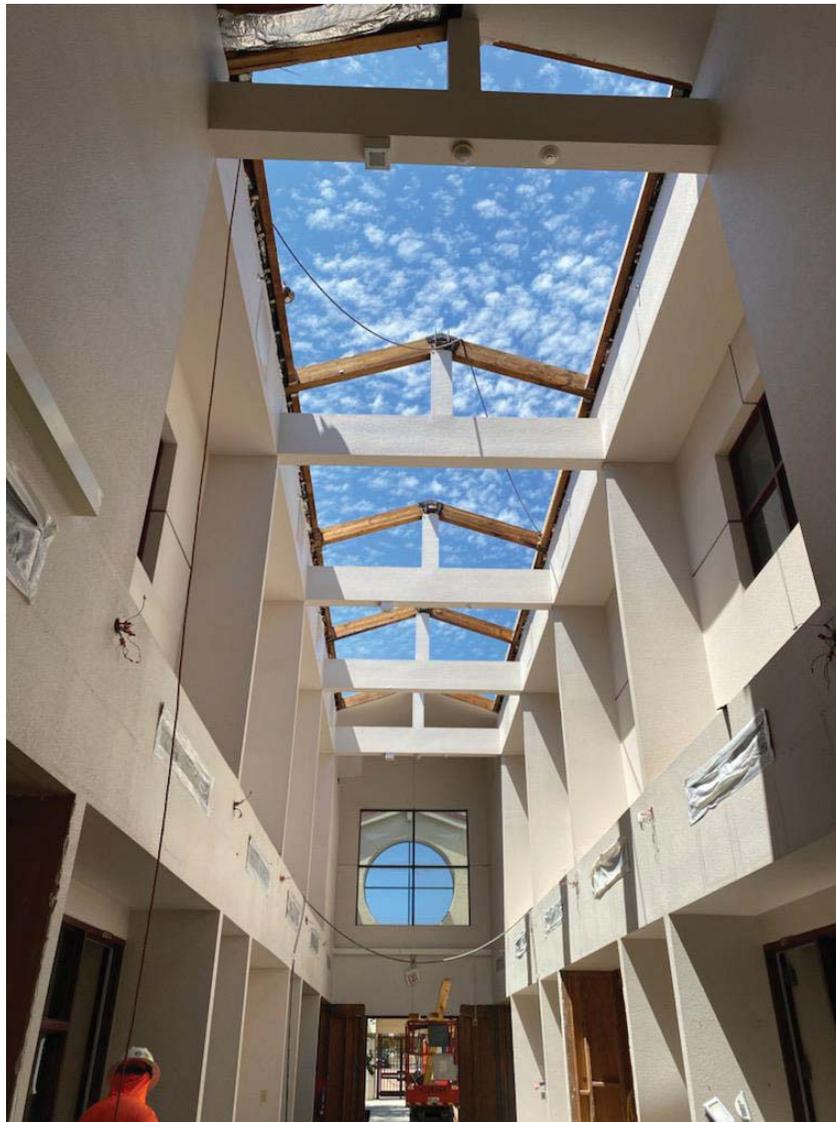



- **Modernization of Butterfield Ranch ES and Hidden Trails ES**

Construction at both sites began October 2021. Buildings B (partial), C, D, E, F, and kitchens are complete. We started Phase 3 Building B, and Phase 4, Building A, on May 30, 2022, and anticipate a project completion date well ahead of the published December 29, 2022 completion date.

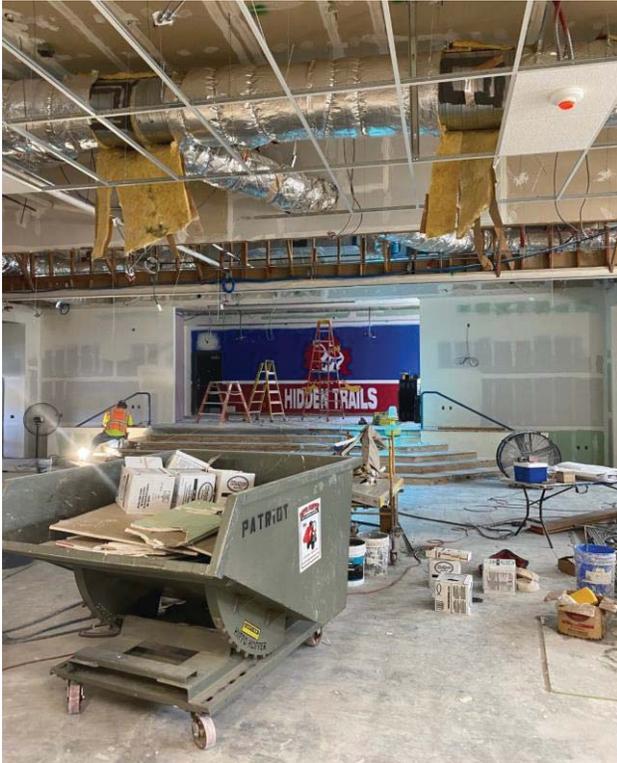

- ***Districtwide Safety and Security Upgrades***

All school sites within the District have been receiving safety and security upgrades for the past two years. The work at these sites includes keyless access controls, single point of entry modifications, additional fencing and gate modifications, security cameras and security alarm upgrades.

The schools have been broken down into project groups and all groups are now 100% complete.

Group 1	Status
Ayala HS	100% complete
Buena Vista HS	100% complete
Chino Hills HS	100% complete
Don Lugo HS	100% complete

Group 2	Status
Cattle ES	100% complete
Litel ES	100% complete
Oak Ridge ES	100% complete
Country Springs ES	100% complete
Rolling Ridge ES	100% complete

Group 3	Status
Magnolia JHS	100% complete
Ramona JHS	100% complete
Woodcrest JHS	100% complete

Group 4	Status
Briggs K-8	100% complete
Cal Aero K-8	100% complete
Borba ES	100% complete
Chaparral ES	100% complete
Cortez ES	100% complete
Dickey ES	100% complete
Liberty ES	100% complete

Group 5	Status
Chino HS (new campus)	100% Complete
Canyon Hills JHS	100% Complete
Townsend JHS	100% Complete

Group 6	Status
Dickson ES	100% complete
Glenmeade ES	100% complete
Marshall ES	100% complete
Newman ES	100% complete
Rhodes ES	100% complete

Group 7	Status
Butterfield Ranch ES	100% Complete
Eagle Canyon ES	100% Complete
Hidden Trails ES	100% Complete
Walnut ES	100% Complete
Wickman ES	100% Complete

Group 8	Status
Adult School	100% Complete
Alternative Education Center	100% Complete
STEAM Allegiance Academy	100% Complete
