


Citizen's Oversight Committee Meeting
Construction Update Overview, May 1, 2024

- ***Chino HS Alterations***

Chino HS Alterations, or Phase 3, is in its final stretch, with an estimated completion of June 2024. The Aquatic Center received new equipment and utility upgrades, grandstands and lighting, and a replastering of the pool, just in time to be turned over to the site for its final swim meets of the year. Construction is still awaiting the installation of the scoreboard. Work continues in both the Frank Elder Gymnasium and the existing locker room, The gymnasium is outfitted with new lighting, HVAC upgrades, and a crucial new storm drain system. This is in addition to the removal of the bleachers and utility upgrades. The existing locker rooms will now house the home and away team locker rooms. They will receive new athletic lockers, restrooms and showers, and utility upgrades. Construction is also providing secured interior and exterior band storage and modernized athletic offices. Lastly, all buildings will receive the necessary ADA improvements.

Chino HS Aquatic Center

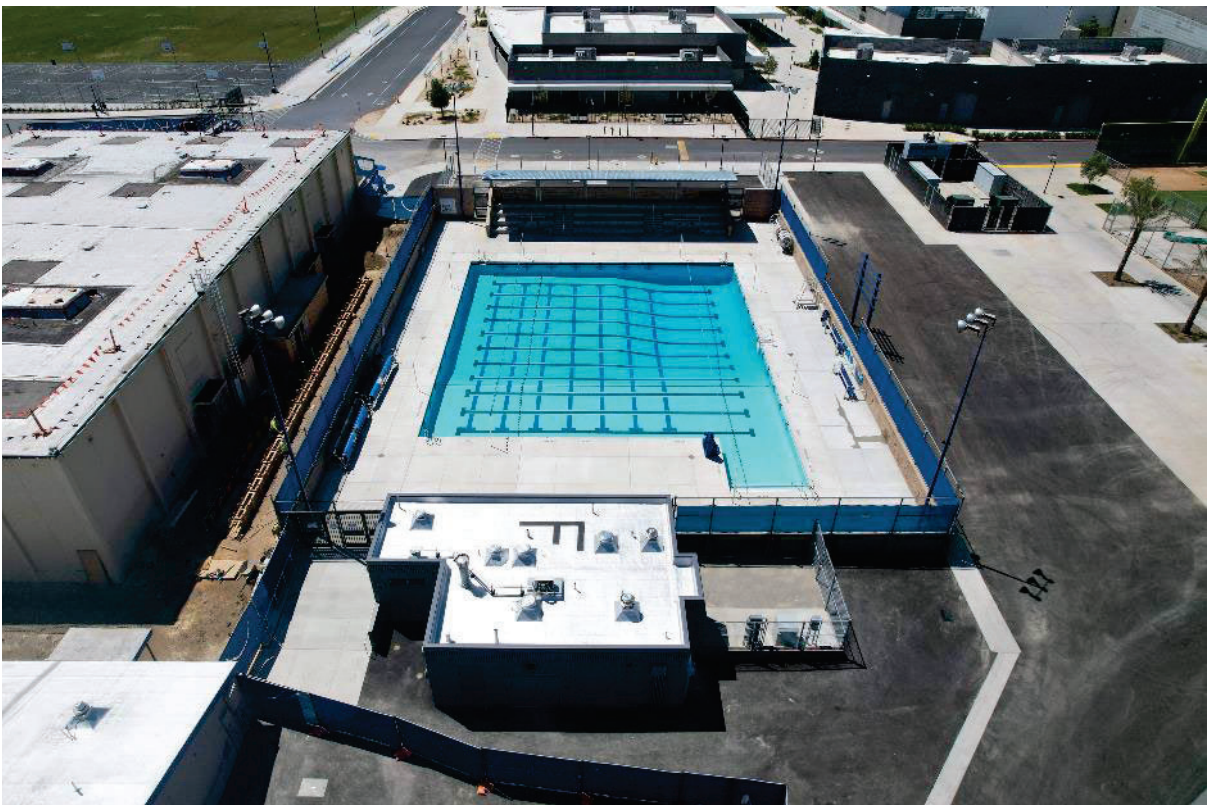


Chino HS Phase 3 Locker Room



- **Eagle Canyon Elementary School Modernization**

Phase 5 is on schedule. This phase consists of the admin office, library, two classrooms, and the removal of the interim housing portables. The installation of finishes, casework, the fire alarm system devices, signage, and exterior painting is ongoing. Completion is anticipated for June 2024.

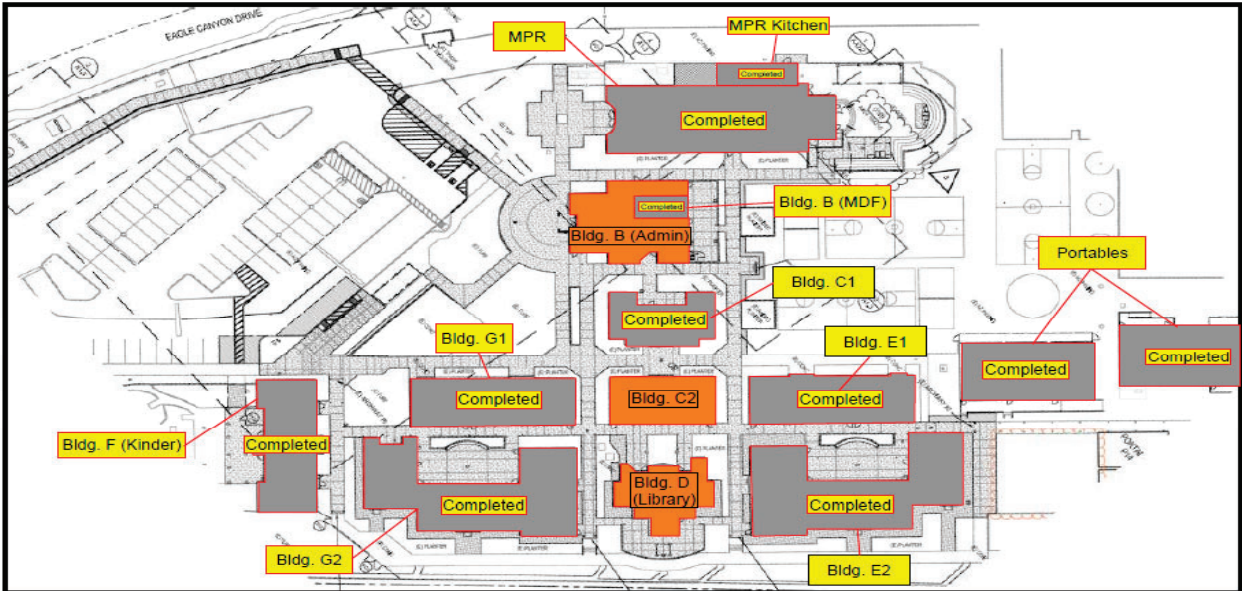

Eagle Canyon Office



Eagle Canyon Library



- **Legacy Academy K8**

The construction of the District's newest school, Legacy Academy K8 is ongoing and scheduled for completion in time for the 2024-2025 school year, which will begin on July 8, 2024. All buildings are receiving final interior finishes, casework, flooring, final paint, glazing and low voltage systems and devices. Final site grading is completed, and exterior sidewalks and concrete is being placed daily. Athletic fields are being prepared for sod and we are currently awaiting the final SCE electrical service connection.



Exterior Hallway



Interior Hallway/Collaboration Space



Legacy Library



Legacy Front Office



- **Front Office Relocations Group A**
 - **Borba, Marshall, and Walnut ES**

Construction is continuing at all three Chino school sites: Borba ES, Marshall ES, and Walnut ES. Exterior building plaster is complete and to be followed by exterior painting. Restroom tile work is underway and will be followed by the installation of plumbing fixtures, ceiling tile and casework. Completion is anticipated in July 2024 which is just in time for the 2024-2025 school year opening.

Walnut ES



Marshall ES



Borba ES



- **Front Office Relocations Group B**
 - **Glenmeade, Litel, and Oak Ridge ES**

Construction is ongoing at all three Chino Hills school sites: Glenmeade ES, Litel ES, and oak Ridge ES. Construction is gearing up for its final months at both Litel and Oak Ridge ES, with our attention on the newly converted office and library spaces, as well as the modernized MPRs. Construction is ongoing in each site's MPR and future library. These sites will also receive a modernized teacher's workroom, staff restrooms, and meeting spaces, all scheduled to be open for the new school year. The brand-new administration building at Glenmeade is also on track to open for the new school year. Framing, roofing, and plastering are all complete making way for HVAC, ducting, and exterior finish installations to begin. Once complete the former administration building will be modernized into the site's library.

Glenmeade ES



Litel ES



Oak Ridge ES



- **Upcoming Shovel-Ready Projects**

- *Don Lugo HS – Construction of New Administration Building, Renovation of Swimming Pool Facility and Kitchen*
- *Multiple School Sites – Electronic Marquees, Shade Shelters and New Furniture*

- **Upcoming Projects in Planning Stages**

- *Glenmeade ES – Kitchen and HVAC Upgrades*
- *Don Lugo HS – Gymnasium Renovation*
- *Ayala HS – Performing Arts Center*
