

CHINO VALLEY UNIFIED SCHOOL DISTRICT
Facilities, Planning, and Operations Division
Greg Stachura, Assistant Superintendent
Phone (909) 628-1201, Ext. 1200 ♦ Fax (909) 548-6034

CITIZENS' BOND OVERSIGHT COMMITTEE

Meeting Minutes

June 4, 2012

Call to Order: Chairman Mike Kreeger called the meeting to order at 5:35 p.m.

Members present were Mike Kreeger, Art Bennett, Sheila Mautz, Roman Nava, Ted Athans, Dave Tennes, Valerie James, and Glenn Duncan. Greg Stachura and Michael Chapko represented District staff.

Mr. Bennett led the group in the Pledge of Allegiance.

1. Public Comment

None.

2. Approval of Minutes from March 5, 2012

Ms. Mautz moved to approve the March 5, 2012 minutes; Ms. James seconded the motion; all members present approved.

3. Expenditure Report for Period ending April 30, 2012

The report for expenditures made during the period ending April 30, 2012 (attached), was distributed to committee members and reviewed by Mr. Stachura. In addition to the bond measure amount of \$150,000,000.00, \$10,387,390.72 in interest was earned as of March 31, 2012; \$950,326.03 was transferred from San Bernardino County for construction of county classrooms, bringing the net total receipts to \$161,337,715.95. \$150,033,943.83 has been spent, leaving a balance of \$11,303,772.12 as of May 31, 2012.

Mr. Stachura said that the Measure M projects are winding down and with everything in the pipeline under construction, by this time next year the bond money will be expended.

4. Report to Board of Education

Mr. Stachura said the meeting minutes will suffice for quarterly reports but the annual report will need to be completed and can be presented to the Board of Education at the June 28th meeting. Ms. James said she will complete the report and Mr. Kreeger will present it to the Board.

5. Advertising for New Members

New members are needed and Julie Gobin will again provide information to the Chino Champion for advertising for parent/guardian, tax advocate, senior citizen, and at large representatives for the committee. A representative for the City of Ontario will also need to be appointed.

6. Meeting Dates

Mr. Kreeger said the committee has been meeting at least quarterly and suggested setting the next two meetings now and the new committee members can decide the other dates later. Members tentatively selected the dates of September 10th and December 3rd at 5:30 p.m.

7. FAR/Planning Update

Mr. Stachura distributed the updated Facilities Assessment Report (FAR) which covers all items on the original list and the status of each item. He said if members have questions about specific items, they should send him an email and he will respond to the questions. If the weather holds out, the Chino Hills High School pool will be ready by January 1st.

8. Construction Update

Mr. Chapko distributed and discussed photos of recently completed and in-progress, Measure M projects and the construction update (attached). Discussion was held regarding the projects, energy conservation, and various issues regarding construction.

9. Member Communications

Members reviewed current events and issues concerning the communities included within the Chino Valley Unified School District boundaries.

10. Other Topics

Meeting was adjourned at 6:31 p.m. The next meeting is scheduled for September 10, 2012.

Attachments: Expenditure Report for Period ending April 30, 2012
 Photos of completed and in-progress Measure M projects
 Construction Update for June 4, 2012
 Facilities Assessment Report, Updated June 2012

ACTIVE CAPITAL FACILITIES PROJECT LIST - Measure M Funded					
Prepared: 6/2012					
		Measure M	OPSC & OTHER	C O M B I N E D	
Project	Facilities Assessment Report Estimates	Budget / Contracted	Received	As of 5/31/12 Expended	Balance
MEASURE M GENERAL EXPENSE					
1. Program Manager - PCM3		2,227,780.32		2,227,780.32	0.00
2. Bond Performance Audit		204,062.36		180,062.36	24,000.00
3. Bond Misc. Cost		94,514.83		63,550.72	30,964.11
4. Legal Fees		12,573.23		12,573.23	0.00
5. CVUSD Payroll		903,195.90		657,058.64	246,137.26
SUBTOTAL	0.00	3,442,126.64		3,141,025.27	301,101.37
NEW CONSTRUCTION - Measure M Match					
1. CHHS	0.00				
2. Preserve	0.00				
3. Rhodes ES	12,400,000.00	6,444,257.23	8,416,259.96	14,860,517.19	0.00
4. Chaparral ES	12,000,000.00	8,811,832.00	7,544,362.14	16,356,194.14	0.00
5. Woodcrest JH	17,200,000.00	14,372,387.28	12,331,223.09	26,703,610.37	0.00
6. Liberty ES	14,500,000.00	9,921,394.06	9,701,147.76	19,622,541.82	0.00
7. Wickman ES	12,200,000.00	5,940,956.37	9,023,621.76	14,964,578.13	0.00
8. Super-Wickman Addition	2,000,000.00	417,127.40	1,487,802.82	1,904,930.22	0.00
	70,300,000.00	45,907,954.34	48,504,417.53	94,412,371.87	0.00
MODERNIZATION PHASE I - Measure M Match					
1. Glenmeade ES	0.00				
2. Magnolia JH	0.00				
3. Don Lugo HS (Red Ph & Bldg A) DM	1,900,000.00	4,249,923.18	6,026,899.42	10,276,822.60	0.00
4. Walnut ES	1,200,000.00	2,286,011.74	2,922,350.88	5,208,362.62	0.00
5. Cortez ES	1,100,000.00	1,375,765.25	3,388,274.16	4,764,039.41	0.00
6. Dickson ES	1,400,000.00	2,009,604.13	2,336,324.51	4,345,928.64	0.00
7. Buena Vista HS	500,000.00	2,799,908.01	1,260,573.10	4,060,481.11	0.00
	6,100,000.00	12,721,212.31	15,934,422.07	28,655,634.38	0.00
MODERNIZATION PHASE II - Measure M Match					
1. Borba ES	0.00	986,159.90	1,474,834.77	2,460,994.67	0.00
2. El Rancho ES DM	400,000.00	798,456.07	1,463,120.66	2,261,576.73	0.00
3. Gird ES DM	500,000.00	747,371.75	1,540,085.98	2,287,457.73	0.00
4. Los Serranos ES DM	400,000.00	696,474.66	1,132,004.22	1,828,478.88	0.00
5. Marshall ES DM	300,000.00	552,244.27	1,094,206.21	1,646,450.48	0.00
6. Newman ES DM	300,000.00	530,914.71	1,166,105.50	1,697,020.21	0.00
7. Ramona JH	700,000.00	1,240,626.94	1,215,466.85	2,456,093.79	0.00
8. Don Lugo HS (Yellow Phase) DM	0.00	1,953,525.26	4,357,195.67	6,310,720.93	0.00
	2,600,000.00	7,505,773.56	13,443,019.86	20,948,793.42	0.00
SUBTOTAL - Projects w/ State Funding	79,000,000.00	66,134,940.21	77,881,859.46	144,016,799.67	0.00
MEASURE M WORK - Fully Measure M Funded					
1. Ayala HS	8,380,361.00	8,727,100.12		8,726,649.28	450.84
2. Walnut ES	6,367,503.00	6,207,567.41	431,428.18	6,638,995.59	0.00
3. Buena Vista HS (MM added to Mod)	1,385,280.00	622,530.23		622,530.23	0.00
4. Cortez ES	1,760,587.00	2,735,866.27		2,735,866.27	0.00
5. Dickson ES	1,464,875.00	2,928,918.17		2,928,918.17	0.00
6. Don Lugo HS (Blue Phase + Ag)	15,541,162.00	22,471,536.00	767,981.46	23,238,685.97	831.49
7. Borba ES	2,179,726.00	21,178.72		21,178.72	0.00
8. El Rancho ES	2,485,974.00	99,391.66		99,391.66	0.00
9. Gird ES	1,509,084.00	231,956.15		230,425.46	1,530.69
10. Los Serranos ES	1,289,896.00	197,389.12		197,389.12	0.00
11. Newman ES	2,055,455.00	358,332.61		356,801.92	1,530.69
12. Marshall ES	5,297,450.00	3,385,443.24		3,383,912.55	1,530.69
13. Ramona JHS (Phase II Mod) Msr M	7,885,431.00	2,707,050.20	829,578.70	3,535,084.54	1,530.66
14. Chino HS	6,438,165.00	13,832,876.50		13,829,876.50	3,000.00
15. Dickey ES	2,023,655.00	1,042,256.92	1,567,461.09	2,598,821.80	10,800.84
16. Canyon Hills JH	3,990,600.00	2,676,880.97		2,676,880.97	0.00
17. Cattle ES	1,236,125.00	4,424,228.38		2,502,858.73	1,921,369.65
18. Townsend JH	1,509,041.00	1,800,965.42		1,800,965.42	0.00
19. Briggs FS	1,414,025.00	5,581,105.31		2,983,265.87	2,597,839.44
20. Butterfield ES	946,998.00	351,738.13		350,515.86	1,222.27
21. Eagle Canyon ES	1,151,450.00	453,825.12		453,825.12	0.00
22. Country Springs	1,927,884.00	936,793.09		935,569.00	1,224.09
23. Glenmeade + (CHS Mod Reimb)	600,533.00	443,961.99	2,695,096.26	460,654.34	2,678,403.91
24. Hidden Trails	194,900.00	210,521.04		210,521.04	0.00
25. Litel	685,937.00	630,404.91		630,404.91	0.00
26. Magnolia JH +(CHS Mod Reimb) + CFD4	3,298,958.00	210,126.22	1,685,273.75	136,402.11	1,673,724.11
27. Oak Ridge ES	1,398,046.00	387,741.16		387,741.16	0.00
28. Rolling Ridge ES	1,736,100.00	735,669.84		734,816.84	853.00
29. Woodcrest JH	1,334,950.00	0.00		0.00	0.00
30. Chino Hills HS	2,205,000.00	7,114,137.27		1,009,624.97	6,104,512.30
				0.00	0.00
SUBTOTAL	89,695,151.00	91,527,492.17	7,976,819.44	84,418,574.12	15,000,354.67
TOTAL MEASURE M BOND PROJECTS	168,695,151.00	161,104,559.02	85,858,678.90	231,576,399.06	15,301,456.04

149,999,999.20 Bonds Issued

10,387,390.72 Interest Earned 3/31/12

950,326.03 Walnut SDC & Campaign

161,337,715.95 Total Receipts

150,033,943.83 Total Expended

11,303,772.12 Cash Balance

as of 5/31/12

11,303,772.12

Facilities Planning Dept. - MP

0.00


AYALA SHADE SHELTER



BRIGGS HVAC & MODERNIZATION

COMPLETED CLASSROOM

ENO BOARD PROJECTOR

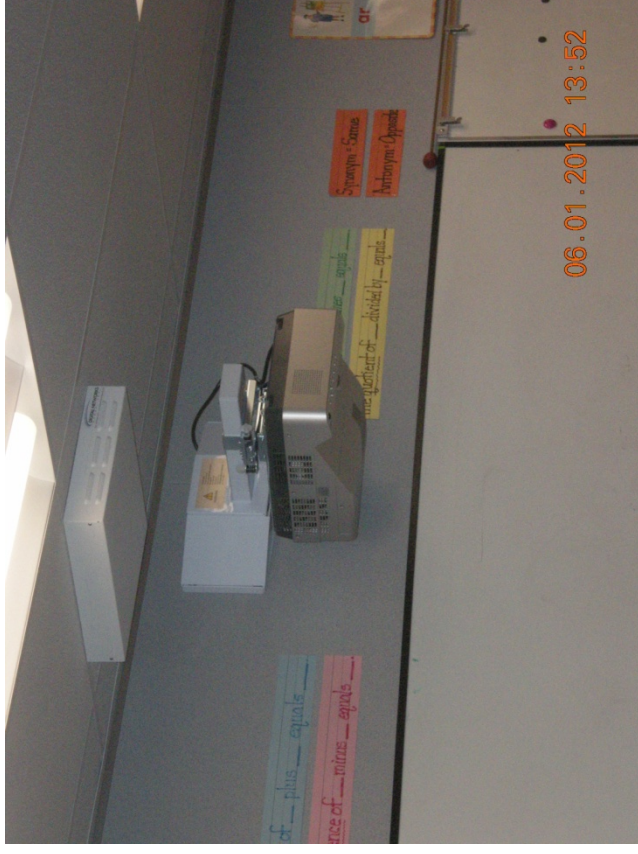

BRIGGS HVAC & MODERNIZATION

NEW TEACHER WORKROOM

NEW HVAC ENERGY REBATE



CATTLE CLASSROOM WING

NEW BUILDING COURTYARD



NEW CLASSROOM CASE WORK



CATTLE CLASSROOM WING

RESTROOM TILE INSTALLATION

ENO BOARD INSTALLATION



CHINO HHS POOL CONSTRUCTION

REINFORCING POOL BOWL



POOL DRAIN INSTALLATION




CHINO HHS POOL CONSTRUCTION

BUILDING PAD # 1



BUILDING PAD #2





Citizen's Oversight Committee Meeting
Construction Update Overview, June 4, 2012
(Updates since March 5, 2011 meeting are in bold)
Prepared and Presented by Bill Childress,
Construction Coordinator

New Classroom Wing Addition at Cattle ES

Contract awarded to PacWest Construction; project began June 30, 2011. Construction period is June 2011 through August 2012. Framing is 98% complete. Interior mechanical, plumbing and electrical work is 99% complete. Exterior stucco work to begin next week and all building should be dried in by March 26, at which time interior drywall work will begin.

The project is 80% complete and still tracking on schedule. Items left to complete include interior building finishes; such as, tackable walls, ceiling tiles, carpet, marker-boards, mechanical/electrical, plumbing finishes, restroom partitions, fixtures and tile.

Exterior work yet to be completed; lunch shelter installation, playground equipment installation, walkway canopy installation, landscaping and irrigation as well as all exterior surfacing and fencing. Project is currently on schedule.

Modernization & HVAC Replacement at Briggs FS

Bids opened June 2, 2011. Contract awarded to Harik Construction, work began July 25, 2011. Construction is on schedule and in the 6th phase with phase 7 scheduled to begin March 17. **90% of class room phases are 100% complete. Work has begun on the final phase where access is possible. Effective June 11, final phase will be in full operation. These areas include, administration offices, cafeteria, restrooms, multipurpose room, library, physical education rooms and kindergarten classrooms. Exterior work to be completed in the final phase includes, shade structure installation, landscaping, site signage and all concrete and asphalt work.**

Swimming Pool at Chino Hills HS

This project was awarded to Construct 1 at the March 15, 2012 Board meeting. A ground breaking ceremony was held and contractor mobilization began April 2, 2012. **Work began April 8, 2012 with completion expected by January 31, 2013. Work is currently on schedule. Underground conduit for utilities is completed in (1) building and partially completed on the other. Forming for the slab over grade is underway for both buildings. The base and vapor barrier is in place on (1) building. The pool shell has been excavated and installation the reinforcing steel to the pool shell is underway. Gunite pour of the pool shell is scheduled in approximately (2) weeks. Power and low voltage lines to the stadium have been completely changed over to the new pathways.**

Interior Modernization Work at Glenmeade ES

This project was Board approved April 5, 2012 and awarded to WCCR Construction. Work will begin June 11 and is projected to take 55 days with completion by August 24, 2012.

Exterior Modernization Work at Glenmeade ES

The project was Board approved April 5, and awarded to WCCR Construction. Work will begin June 11, 2012 and is projected to take 55 days with completion by August 24, 2012.

Magnolia Junior High School Modernization & Library Renovation

Although originally a Measure M project, adequate funding was not be available to complete begin project and it was temporarily shelved. Funding from CFD4 will be utilized to cover the cost of this project. The project is scheduled to be awarded at the June 14, 2012 Board meeting, with construction expected to begin by late June, 2012.

STATUS			
PLANNING	IN PLANNING PHASE		
DSA	AT DSA / PLAN REVIEW		
BID	CURRENTLY BIDDING		
IN PROG	UNDER CONSTRUCTION		
COMP	COMPLETED		
NO ISSUES	NO ISSUES / SHIFTED PRIORITIES		
X	PENDING FUNDING		
PRIORITY / RANK RECOMMENDATIONS			
1	NEW CONSTRUCTION FOR GROWTH NEEDS		
2	HEALTH & SAFETY ISSUES		
3	INFRASTRUCTURE REPAIR/STRUCTURAL INTEGRITY/ENERGY CONSERVATION		
4	UPGRADE/RENOVATE CLASSROOMS		
5	SITE IMPROVEMENTS/PROGRAM ENHANCEMENTS		
6	FURNITURE/EQUIPMENT FOR INSTRUCTION		
Borba Fundamental - Reopened as Chino Valley Adult School			
1952 2007-08 MODERNIZATION			
	RANK	PRIORITY	STATUS
A	2	Revise and expand parking and student drop-off zones to reduce safety hazards.	NO ISSUE
B	2	Install monitored security system phones in classrooms.	COMP 2010
C	2	Add exterior lighting for safety and security.	COMP 2009
D	3	Repair dry rot/moisture damage – Kindergarten.	COMP 2004
E	3	Repair rusted plumbing pipes and fixtures.	COMP 2007
F	4	Renovate aging classrooms and multipurpose room.	COMP 2007
G	5	Expand student service areas (school office and nurse's office).	COMP 2007
Briggs Fundamental			
1988 2011 MODERNIZATION			
	RANK	PRIORITY	STATUS
A	2	Update exterior lighting for safety.	COMP 2009
B	3	Updated electrical wiring and plumbing in all of the classrooms.	IN PROG
C	3	Replace or repair leaky roofs.	IN PROG
D	3	Repair covered walkways throughout the school.	COMP 2005
E	5	Extra classroom for a computer lab and future student growth.	IN PROG
F	5	Five specialized classrooms for labs and elective classes.	IN PROG
G	5	Extra sidewalks, planters, and cement work.	IN PROG
H	5	Larger workspace for staff.	IN PROG
I		Renovate air conditioning and ventilation systems for energy efficiency.	IN PROG
Butterfield Ranch Elementary			
1989			
	RANK	PRIORITY	STATUS
A	2	Install covered shade area.	COMP 2010
B	5	Upgrade electrical service in classrooms for access to technology.	COMP 2010
C	5	Create specialized instructional space.	NO ISSUE
D	5	Install covered walkways throughout the school.	X
E	5	Expand and upgrade hard space area for safety.	COMP 2010
F	6	Replace playground equipment for safety.	COMP 2009
Cattle Elementary			
1991			
	RANK	PRIORITY	STATUS
A	2	Revise parking zones/bus zones for safety and security reasons.	COMP 2009
B	4	Replace seven older portable classrooms / build new classroom wing	IN PROG
C	5	Construct multi-use room with computer lab capabilities.	X
D	5	Remodel/expand teacher preparation work area to provide more counter and storage space due to the increase in the number of teaching staff.	X
E	6	Additional equipment for outside play areas.	IN PROG

Cortez Elementary			
1978 2006-07 MODERNIZATION			
	RANK	PRIORITY	STATUS
A	2	Update/repair public address, emergency, and fire communication systems.	COMP 2006
B	2	Install telephones in each classroom.	COMP 2006
C	4	Install additional relocatable classrooms.	COMP 2003
D	4	Install/repair adequate electrical wiring and outlets in classrooms.	COMP 2006
E	5	Build storage space to house supplies and off-track materials and cabinets.	COMP 2006
F	5	Build enclosed eating area (cafeteria) for students.	COMP 2006
G	5	Purchase and install portable to house library/computer lab.	NO ISSUE
H	5	Construct/enlarge additional student and adult restrooms.	COMP 2006
I		Renovate front office and work spaces	COMP 2008
Country Springs Elementary			
1994			
	RANK	PRIORITY	STATUS
A	2	Change sand to wood chips in playground equipment area.	COMP 2011
B	2	Revise student drop-off zones to reduce safety hazards.	COMP 2010
C	3	Renovate air conditioning and ventilation systems for energy efficiency.	COMP 2010
D	3	Replace deteriorated ceiling tiles.	COMP 2006
E	4	Upgrade telephone and communication systems.	COMP 2010
F	5	Renovate and expand library.	COMP 2010
G	5	Construct access ramps and walkways to main buildings. Add stairs on the north and south of campus for ease of access.	COMP 2010
H	5	Raise kindergarten fence.	COMP 2009
I	5	Cabinets with counter tops built into permanent portable classrooms.	NO ISSUE
J	5	Provide permanent outdoor covered eating area.	COMP 2010
K	5	Enlarge parking lot.	NO ISSUE
Dickey Elementary			
1981 2008-2009 MODERNIZATION			
	RANK	PRIORITY	STATUS
A	2	Remodel all restrooms.	COMP 2010
B	4	Install telephones in all classrooms.	COMP 2009
C	5	New staff lounge to accommodate a staff of 50+.	COMP 2009
D	5	Enlarge and expand parking lot.	COMP 2009
E	5	Install new playground equipment in kindergarten playground.	COMP 2009
F	5	Remove existing computer area partitions between classrooms and media center and replace with walls to reduce noise.	COMP 2009
G	5	Remodel and enlarge cafeteria and kitchen with new tables and benches to accommodate 1000.	COMP 2009
H	5	New staff workroom, renovate front office and work spaces	COMP 2009
I	6	Replace existing curtains.	COMP 2009

Dickson Elementary			
1978 2006-07 MODERNIZATION			
	RANK	PRIORITY	STATUS
A	3	Repair roof leaks.	COMP 2004
B	3	Repair water damaged ceilings, floors and walls.	COMP 2004
C	3	Replace wooden foundations, building frames, etc.	NO ISSUE
D	3	Paint outside buildings.	COMP 2006
E	4	Install adequate electrical service and outlets in classrooms.	COMP 2006
F	5	Covered/enclosed eating area.	COMP 2006
G	5	Install covered walkways from portables located a distance from main building.	X
H	5	Additional space for parent workshops, counseling, school programs, etc.	COMP 2006
I		Renovate front office and work spaces	COMP 2008
Eagle Canyon Elementary			
1987			
	RANK	PRIORITY	STATUS
A	2	Replace sand under playground equipment with compliant material.	COMP 2011
B	3	Repair roof leaks.	COMP 2010
C	3	Replace old lunch tables and playground benches.	COMP 2009
D	3	Repair load-carrying beam in Multipurpose Room so that the folding wall becomes functional again.	COMP 2008
E	4	Replace intercom system and old telephone system.	COMP 2010
F	4	Replace public address system in the Multipurpose Room.	COMP 2010
G	5	Widen front gates for additional traffic exit lane.	X
H	5	Increase blacktop play area to recover area lost to portable classrooms.	NO ISSUE
I	5	Walk-through gate and entry stairs from Eagle Canyon Drive.	X
J	5	Create staff parking area for 8 to 10 cars behind rooms 28 and 29.	X
K	5	Expand teacher's workroom area using adjacent unused patio.	X
L	5	Extend walkway covering to include new portables.	X
M	5	Extend overhead cover in student outside eating area.	X
N	6	Replace outdated classroom computers.	TECH DEPT.
O	6	Replace worn classroom/office furniture.	X
EI Rancho Elementary - CLOSED			
1951 2007-08 MODERNIZATION			
	RANK	PRIORITY	STATUS
A	2	Provide permanent covered eating area outside.	COMP 2006
B	2	Remove and replace playground equipment for safety.	NO ISSUE
C	2	Add exterior lighting to meet safety standards.	COMP 2009
D	2	Revise student drop-off zone in front of school to reduce safety hazards.	NO ISSUE
E	3	Replace clogged pipes and plumbing system.	NO ISSUE
F	4	Install adequate electrical service and outlets in classrooms.	COMP 2007
G	4	Remodel interiors of bathrooms, including fixtures.	COMP 2007
H	4	Renovate Multipurpose room; redo stage, food service area, lighting and lowered ceiling.	COMP 2007
I	4	Renovate kindergarten classrooms (two permanent structures).	COMP 2007
J	5	Install covered walkway.	X

Gird Elementary - Reopened as Borba			
1953 2007-08 MODERNIZATION (PARTIAL CAMPUS)			
	RANK	PRIORITY	STATUS
A	2	Remodel interiors of restrooms, including fixtures.	COMP 2011
B	2	Repair uneven/eroded surfaces on playgrounds for safety.	COMP 2009
C	2	Add exterior lighting to meet safety standards.	COMP 2009
D	3	Paint exterior and interior of site.	COMP 2008
E	4	Reconfigure and renovate cafeteria and kitchen area.	COMP 2007
F	5	Improve drainage and re-landscape.	COMP 2009
G	5	Increase office space and student service areas.	COMP 2007
H	5	Create specialized instructional space.	COMP 2007
I	6	Computers for classrooms/computer lab, laptops for Power Point presentations and programs.	COMP 2007
Glenmeade Elementary			
1969 MODERNIZED IN 2003 CAMPUS-WIDE			
	RANK	PRIORITY	STATUS
A	2	Security alarm system.	
B	2	Enclose fence to secure campus.	COMP 2010
C	5	Enclose covered eating area.	PLANNING
D	5	Re-landscape grounds and renovate irrigation system to improve drainage.	IN PROG
E	5	Remodel/expand teacher preparation area to provide counter and storage space.	IN PROG
F	5	Replace movable walls.	IN PROG
G	5	Replace old Plexiglas with glass.	IN PROG
H	5	Concrete walkway on top playground at bus pick-up and drop-off.	IN PROG
I	6	Replace old desks and chairs (classrooms).	
Hidden Trails			
1995			
	RANK	PRIORITY	STATUS
A	1	Portable kindergarten room.	NO ISSUE
B	2	Security fences.	COMP 2011
C	5	Expand parking lot.	NO ISSUE
D	6	Replace all chalkboards with electronic white boards.	COMP 2010
Litel Elementary			
1987			
	RANK	PRIORITY	STATUS
A	2	Revise parking and student drop-off zones to reduce safety hazards.	COMP 2010
B	2	Add exterior lighting.	COMP 2010
C	5	Install water to seven portables.	COMP 2010
D	5	Install wiring for telephone service for all classrooms.	COMP 2010
E	5	Additional portable for computer lab.	NO ISSUE
F	5	Increase size of eating area overhang and install weatherproof, drop-down vinyl enclosure.	X
G	5	Add covered walkways to portables.	X
H	6	Replacement of chalkboards with white boards.	X
I	6	New computers with CD Rom for the classrooms.	COMP 2009

Los Serranos Elementary - Reopened as Alternative Ed Center			
1962	2007-08 MODERNIZATION		
	RANK	PRIORITY	STATUS
A	2	Security alarm system for selected buildings.	
B	2	Remove and replace all some cracked concrete walkways – safety concern.	COMP 2011
C	2	Improve drop-off/pick-up zone in parking lot.	COMP 2006
D	3	Remove/replace damaged and broken bathroom stalls and doors.	COMP 2007
E	3	Repair and/or replace leaking hallway awnings and extend awnings to include uncovered walkway to upper ramps.	COMP 2008
F	4	Install additional electrical outlets in classrooms for technology.	COMP 2007
G	4	Enlarge and reconfigure office area for safety and security of entire population. Need better positioning for security of school entrance.	COMP 2008
H	5	Install phones in all classrooms for teacher/student safety.	COMP 2010
I	5	Install awnings/overhead covering for portables and rooms 24, 30 and 31.	NO ISSUE
Marshall Elementary			
1963	2007-08 MODERNIZATION		
	RANK	PRIORITY	STATUS
A	2	Extend parking area to alleviate safety hazards.	COMP 2006
B	2	Renovate restrooms.	COMP 2011
C	3	Upgrade electrical systems in classrooms.	COMP 2007
D	4	Modernize 20's wing, rooms 30 – 32.	COMP 2007
E	4	Upgrade fire, public address, security, and communications systems.	COMP 2007
F	5	Remodel/expand teacher preparation area to provide counter and storage area.	X
G	5	Increase office space and student service areas.	X
H	5	Expand library.	COMP 2007
I	5	Construct permanent classrooms (10).	COMP 2009
Newman Elementary			
1953	2007-08 MODERNIZATION		
	RANK	PRIORITY	STATUS
A	2	Upgrade restrooms.	COMP 2011
B	3	Repaint entire school.	COMP 2010
C	4	Upgrade public address system.	COMP 2007
D	4	Modernize Rooms 25 – 33.	COMP 2007
E	5	Upgrade water line system.	COMP 2009
F	5	Upgrade main asphalt areas.	COMP 2007
G	5	Install outside covered eating area.	COMP 2006
Oak Ridge Elementary			
1988			
	RANK	PRIORITY	STATUS
A	2	Additional security fencing/gates.	COMP 2011
B	3	Repair cracks in existing foundation.	COMP 2009
C	3	Repair/replace water damaged ceiling tiles.	COMP 2010
D	4	Upgrade communications systems for school-wide use.	COMP 2010
E	4	Replace existing carpeting.	COMP 2009
F	5	Increase capacity of Media center.	NO ISSUE
G	5	Replace existing skylights.	COMP 2010
H	5	Re-landscape grounds to improve drainage/erosion areas and provide shade.	COMP 2010
I	5	Install covered walkways.	X

Rolling Ridge Elementary			
1989			
	RANK	PRIORITY	STATUS
A	2	Sidewalk in parking lot area from stairs to entrance (safe exit to north).	COMP 2010
B	3	Replace/repair tile and carpet in Media Center.	COMP 2009
C	4	Install phones in every classroom.	COMP 2010
D	5	Extend perimeter chain link fences from 6 feet to 10 feet separating the field/slope and playground.	COMP 2009
E	5	Additional classrooms to accommodate classroom, music and library.	NO ISSUE
F	5	Develop empty field area on the south end of playground.	NO ISSUE
G	5	Renovate air conditioning/heating.	COMP 2011
H	5	Add trees to playground for shade.	COMP 2010
Walnut Elementary			
1969, 2006 06-07 MODERNIZATION (CAMPUS-WIDE)			
	RANK	PRIORITY	STATUS
A	1	Additional portables to allow school to return to standard track.	COMP 2006
B	2	Install covered outdoor eating area.	COMP 2006
C	2	Revise parking and student and bus drop-off zones to reduce safety hazards.	COMP 2006
D	3	Repair covered walkways.	COMP 2006
E	4	Renovate aging buildings, 38 classrooms, MPR, 8 restrooms + 4 kindergarten, 7 small specialty rooms.	COMP 2006
F	5	Provide computer lab.	COMP 2006
G	5	Build additional student restrooms.	COMP 2006
H	5	Remodel/enlarge office and student service areas.	COMP 2006
I	5	Provide coverings for Rooms 35-41 for protection from inclement weather.	COMP 2006
Canyon Hills Junior High			
1991			
	RANK	PRIORITY	STATUS
A	1	Construct 3+ permanent classrooms.	NO ISSUE
B	3	Install new ceiling tiles.	COMP
C	4	Remodel science classrooms installing two lab stations.	COMP 2010
D	5	New lockers in locker rooms.	COMP 2007
E	5	Create specialized instructional and meeting space.	COMP 2010
F	5	Add adult restrooms in English channel.	COMP 2010
G	5	Reconfigure library and computer lab for large group instruction.	COMP 2010
Magnolia Junior High			
1967 2003 MODERNIZATION (FULL CAMPUS)			
	RANK	PRIORITY	STATUS
A	2	Update security (\$2.39/Sq.Ft.), communication (\$2.18/Sq.Ft.), and bell systems.	COMP 2010
B	2	Repair exterior lighting, motion detectors, accessible by site administrator.	COMP 2008
C	3	Replace portable classrooms.	COMP 2005
D	5	Provide covered eating area.	X
E	5	Install covered walkways throughout the school.	X
F	5	Increase office space and student service areas.	COMP 2005
G	5	Remodel library.	IN PROG
H	5	Remodel/expand teacher preparation area to provide counter and storage space.	IN PROG

Ramona Junior High			
1965		1992-93; 2007-08 MODERNIZATION (PARTIAL CAMPUS)	
	RANK	PRIORITY	STATUS
A	2	Update emergency/public address/communication system throughout school.	COMP 2007
B	2	Add exterior lighting for safety.	COMP 2009
C	3	Construct permanent classrooms.	COMP 2009
D	3	Repair antiquated plumbing and sewer system.	NO ISSUE
E	3	Renovate air conditioning system.	COMP 2008
F	3	Remove asbestos and dry rot.	COMP 2009
G	5	Renovate and expand existing locker room facilities.	COMP 2009
H	5	Upgrade electrical wiring and outlets.	COMP 2007
I	5	Install covered walkways throughout the school.	X
Townsend Junior High			
1986			
	RANK	PRIORITY	STATUS
A	2	Repair uneven and unsafe ground surfaces.	COMP 2010
B	3	Repair leaky roofs and deteriorated ceiling tiles.	COMP 2008
C	3	Repair covered walkways throughout the school.	COMP 2010
D	4	Update telephone and communication systems for safety.	COMP 2010
E	5	Create specialized instructional space.	COMP 2010
F	5	Install wiring for access to technology.	COMP 2010
G	5	Add computer/technology lab for students.	COMP 2010
H	5	Reconfigure library and computer lab for large group instruction.	COMP 2010
Woodcrest Junior High			
2005		NEW CONSTRUCTION	
	RANK	PRIORITY	STATUS
A	2	Add exterior lighting for safety and security.	COMP 2005
B	2	Peepholes for security.	NO ISSUE
C	2	Renovate student restrooms, including fixtures.	COMP 2005
D	3	Repair worn-out and unsafe flooring.	COMP 2005
E	5	Add storage space.	COMP 2005
F	5	Resurface the site.	COMP 2005
G	5	Expand PE locker rooms.	COMP 2005
H	5	Replace drinking fountains.	COMP 2005
I	5	Expand library to accommodate increasing student population.	COMP 2005
Ayala High			
1990			
	RANK	PRIORITY	STATUS
A	2	Revise parking zones to reduce safety hazards.	COMP 2010
B	3	Repair leaky roofs.	COMP 2005
C	3	Renovate heating and air conditioning systems.	COMP 2010
D	5	Stadium with seating for 5,000 people, artificial turf and synthetic track	COMP 2004
E	5	Provide covered eating area and outside shelter.	COMP 2012
Buena Vista High			
1978		2006-07 MODERNIZATION CAMPUS-WIDE	
	RANK	PRIORITY	STATUS
A	3	Paint and weatherproof entire school.	COMP 2007
B	3	Replace drinking fountains.	COMP 2007
C	5	Patio cover for quad/eating area.	COMP 2007
D	5	Reconfigure Children's Center playground and install equipment.	COMP 2007
E	5	Add a portable science classroom with lab station.	COMP 2010
F	5	Upgrade and expand athletic facilities.	NO ISSUE
G	5	Remodel and expand library	COMP 2007
H	5	Install marquee.	X

Chino High			
1954	2008-2009 MODERNIZATION (PARTIAL CAMPUS)		
	RANK	PRIORITY	STATUS
A	2	Revise parking zone to reduce safety hazards.	COMP 2010
B	2	Reconfigure office area for safety and security.	COMP 2010
C	3	Replace portable classrooms due to dry rot damage.	COMP 2006
D	5	Renovate stadium facilities, artificial turf and synthetic track	COMP 2009
E	5	Add science classrooms with lab stations.	COMP 2008
F	5	Provide covered eating area outside.	X
G	5	Provide covered walkways through the school.	X
H	5	Build additional classroom and storage space for music program.	COMP 2009
Chino Hills High			
2001, 2003			
	RANK	PRIORITY	STATUS
A	2	Security system.	COMP 2003
B	5	Library books.	X
C	5	Renovate stadium facilities, artificial turf and synthetic track	COMP 2009
D		Construct swimming pool	IN PROG
Don Lugo High			
1972, 2006	2004-08 MODERNIZATION (FULL CAMPUS)		
	RANK	PRIORITY	STATUS
A	2	Renovate existing restrooms and locker rooms, including flooring, toilets, stalls, and fixtures.	COMP 2008
B	2	Add exterior lighting for security and safety.	COMP 2009
C	3	Upgrade electrical wiring and outlets.	COMP 2007
D	3	Renovate drainage system to alleviate flooding.	COMP 2007
E	3	Paint school uniform colors.	COMP 2003
F	4	Construct permanent classrooms (30 portable buildings).	COMP 2007
G	5	Add science classrooms with adequate lab workstations.	COMP 2007
H	5	Increase office space and student service areas.	COMP 2007
I	5	Install covered shade area.	COMP 2007
J	5	Upgrade and expand athletic facilities, including gym foyer and construction of new football stadium, artificial turf and synthetic track	COMP 2010
